(Rule 116)

Measurement Book

No. B

188816

..... No. .....

..... of Work ..... From ..... To .....

..... of Contractor of nature of Agency .....

..... of commencement of work ..... I & F Final Bill

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
2	Number 3	Length 4	Breadth 5	Depth 6	7	8
Name of work - Emergency works in ward No. 13, Mallasandra Shettyhalli sub division.						
Estimate cost - Rs 20.00 Lakh.						
Job code - 013-20-000005						
Admin Sanction - EE/DD/AS/17/2021 dated					22.04.2020	
Technical Sanction - EE/DD/TS/01/2021 dated					22.04.2020	
Work order - No EE/DD/001/130/2020-21 dated					19.11.2020	
Agency - Sri Mahadeva Naik.						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
Sheet							
	1) Coarse sand excavation by mixed vehicles for basement & shoulder						
	Qty approximately		1144.35 m³ @ 192.95/-				220765.42
	2) Providing and laying Reinforced cement concrete in foundation & plinth beam including centering & shuttering						
	Qty approximately		18.00 m³ @ 4820.66/-				86771.88
	3) Providing and laying plain/R.C.C. for footings, any size, under water including dewatering, curing, cost of all materials, labour charges etc complete						
	Qty approximately		54.00 m³ @ 6290.74/-				339718.92
	4) Providing TMT steel including for R.C.C. work including bending, cutting,						
	bent						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 488847

Serial No. .....
Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	bending, hooking, placing for footing, Capping and shaft using mixed steel						
	Qty approximately		3.89 m³ @ 63286/-				246152.97
	5) Providing and laying R.C.C. work of 450 mm thick for column, made of 20 mm thick formwork made of Qty approximately steel —						
	Qty approximately		71.33 m² @ 3214.75/-				229436.71
	6) Providing & laying R.C.C. work in slabs of roofing, sunshade & landing including 1:1½:3 mix proportion, including all labour charges complete —						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	RCC ಛಾವಣಿ ಚಾನಲ್	261	1/2	1413.12	—		3608243
					GST 12%		1491700.13
	Conclude				total		1790040.2
	1) Contract limit the work to be executed by						1670704.4
	2) There no Segregated Deeds by				ಕಿರಿಯ ಅಭಿಯಂತರರು		1491680.84
					05/02/2021		1790040.2
							1670683

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

1670683

Audited and admitted for Rs. 1670683-00

Passed by Cheque for Rs. 1504428-00

(Rupees Fifteen Lakh Four thousand Four hundred Twenty Eight only)

Serial No. 166255-00

Name of Work

Name of Contractor or nature of Agency

Date of commencement of work

Accounts Superintendent

M. A. R. 57 (Rule 1
Measurement Book

No. B 188816

From To

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
	2	3	4	5	6	7	8

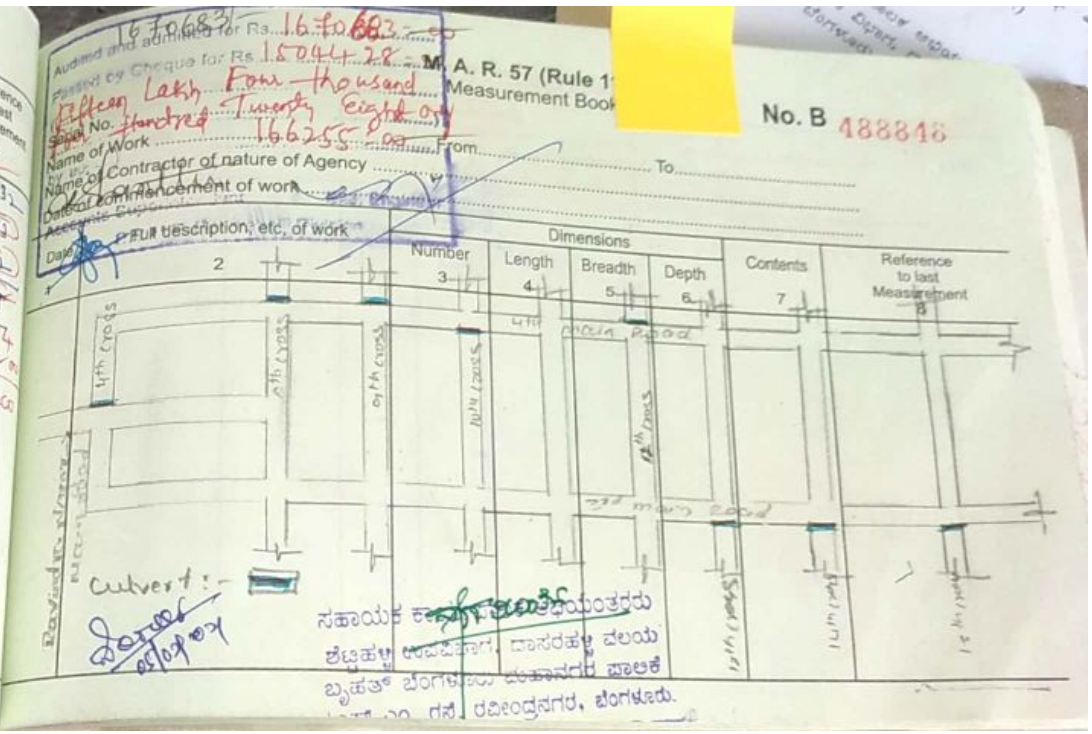

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Scanned by CamScanner
